ID		Task Name	Duration	Start	Finish
1		**Port Orchard Overlay/Replacment**	**150 days**	**Wed 9/28/11**	**Fri 5/4/12**
2		Notice to Proceed	0 days	Wed 9/28/11	Wed 9/28/11
3		**SCH A - SEDGWICK AT LOWES**	**10 days**	**Mon 10/17/11**	**Fri 10/28/11**
4		Install CB Inserts	1 day	Mon 10/17/11	Mon 10/17/11
5		Reference Existing Pavement Markings	1 day	Mon 10/17/11	Mon 10/17/11
6		Pavement Repair	2 days	Tue 10/18/11	Wed 10/19/11
7		Plane Existing HMA	1 day	Thu 10/20/11	Thu 10/20/11
8		HMA Overlay	1 day	Fri 10/21/11	Fri 10/21/11
9		Install Induction Loops	1 day	Mon 10/24/11	Mon 10/24/11
10		Adjust Utilities	2 days	Tue 10/25/11	Wed 10/26/11
11		Roadway Striping	2 days	Thu 10/27/11	Fri 10/28/11
12		**SCH D - LIPPERT & SIDNEY**	**10 days**	**Tue 10/18/11**	**Mon 10/31/11**
13		Install CB Inserts	1 day	Tue 10/18/11	Tue 10/18/11
14		Reference Existing Pavement Markings	1 day	Tue 10/18/11	Tue 10/18/11
15		Plane Existing HMA	1 day	Fri 10/21/11	Fri 10/21/11
16		HMA Overlay	1 day	Mon 10/24/11	Mon 10/24/11
17		Roadway Striping	1 day	Mon 10/31/11	Mon 10/31/11
18		**SCH E - SIDNEY TO SOUTH ST**	**108 days**	**Wed 10/19/11**	**Wed 3/28/12**
19		Install CB Inserts	1 day	Wed 10/19/11	Wed 10/19/11
20		Reference Existing Pavement Markings	1 day	Wed 10/19/11	Wed 10/19/11
21		Pavement Repair	2 days	Tue 10/25/11	Wed 10/26/11
22		Plane Existing HMA	1 day	Thu 10/27/11	Thu 10/27/11
23		HMA Overlay	1 day	Fri 10/28/11	Fri 10/28/11
24		Roadway Striping	1 day	Tue 11/1/11	Tue 11/1/11
25		**Project Suspension for Weather**	**98 days**	**Wed 11/2/11**	**Wed 3/28/12**
26		Project Suspension for Weather	98 days	Wed 11/2/11	Wed 3/28/12
27		**SCH B - SEDGWICK AT GLENWOOD**	**27 days**	**Thu 3/29/12**	**Fri 5/4/12**
28		Install CB Inserts	1 day	Thu 3/29/12	Thu 3/29/12
29		Reference Existing Pavement Markings	1 day	Thu 3/29/12	Thu 3/29/12
30		Reference Existing Monument	1 day	Fri 3/30/12	Fri 3/30/12
31		Roadway Excavation	3 days	Mon 4/2/12	Wed 4/4/12
32		Install Geogrid	2 days	Thu 4/5/12	Fri 4/6/12
33		Place CSTC	4 days	Thu 4/5/12	Tue 4/10/12
34		Place HMA	1 day	Wed 4/11/12	Wed 4/11/12
35		Adjust Utilities	1 day	Thu 4/12/12	Thu 4/12/12
36		Roadway Striping	2 days	Fri 4/13/12	Mon 4/16/12
37		**SCH C - S. KITSAP BLVD**	**26 days**	**Fri 3/30/12**	**Fri 5/4/12**
38		Install CB Inserts	1 day	Fri 3/30/12	Fri 3/30/12
39		Reference Existing Pavement Markings	1 day	Fri 3/30/12	Fri 3/30/12
40		Plane Existing HMA	3 days	Wed 4/11/12	Fri 4/13/12
41		Roadway Excavation	2 days	Mon 4/16/12	Tue 4/17/12
42		Place Gravel Base	2 days	Wed 4/18/12	Thu 4/19/12
43		Place CSTC	2 days	Fri 4/20/12	Mon 4/23/12
44		HMA Patching	1 day	Tue 4/24/12	Tue 4/24/12
45		HMA Overlay	1 day	Wed 4/25/12	Wed 4/25/12
46		Install Induction Loops	1 day	Thu 4/26/12	Thu 4/26/12
47		Adjust Utilities	2 days	Fri 4/27/12	Mon 4/30/12
48		Roadway Striping	4 days	Tue 5/1/12	Fri 5/4/12

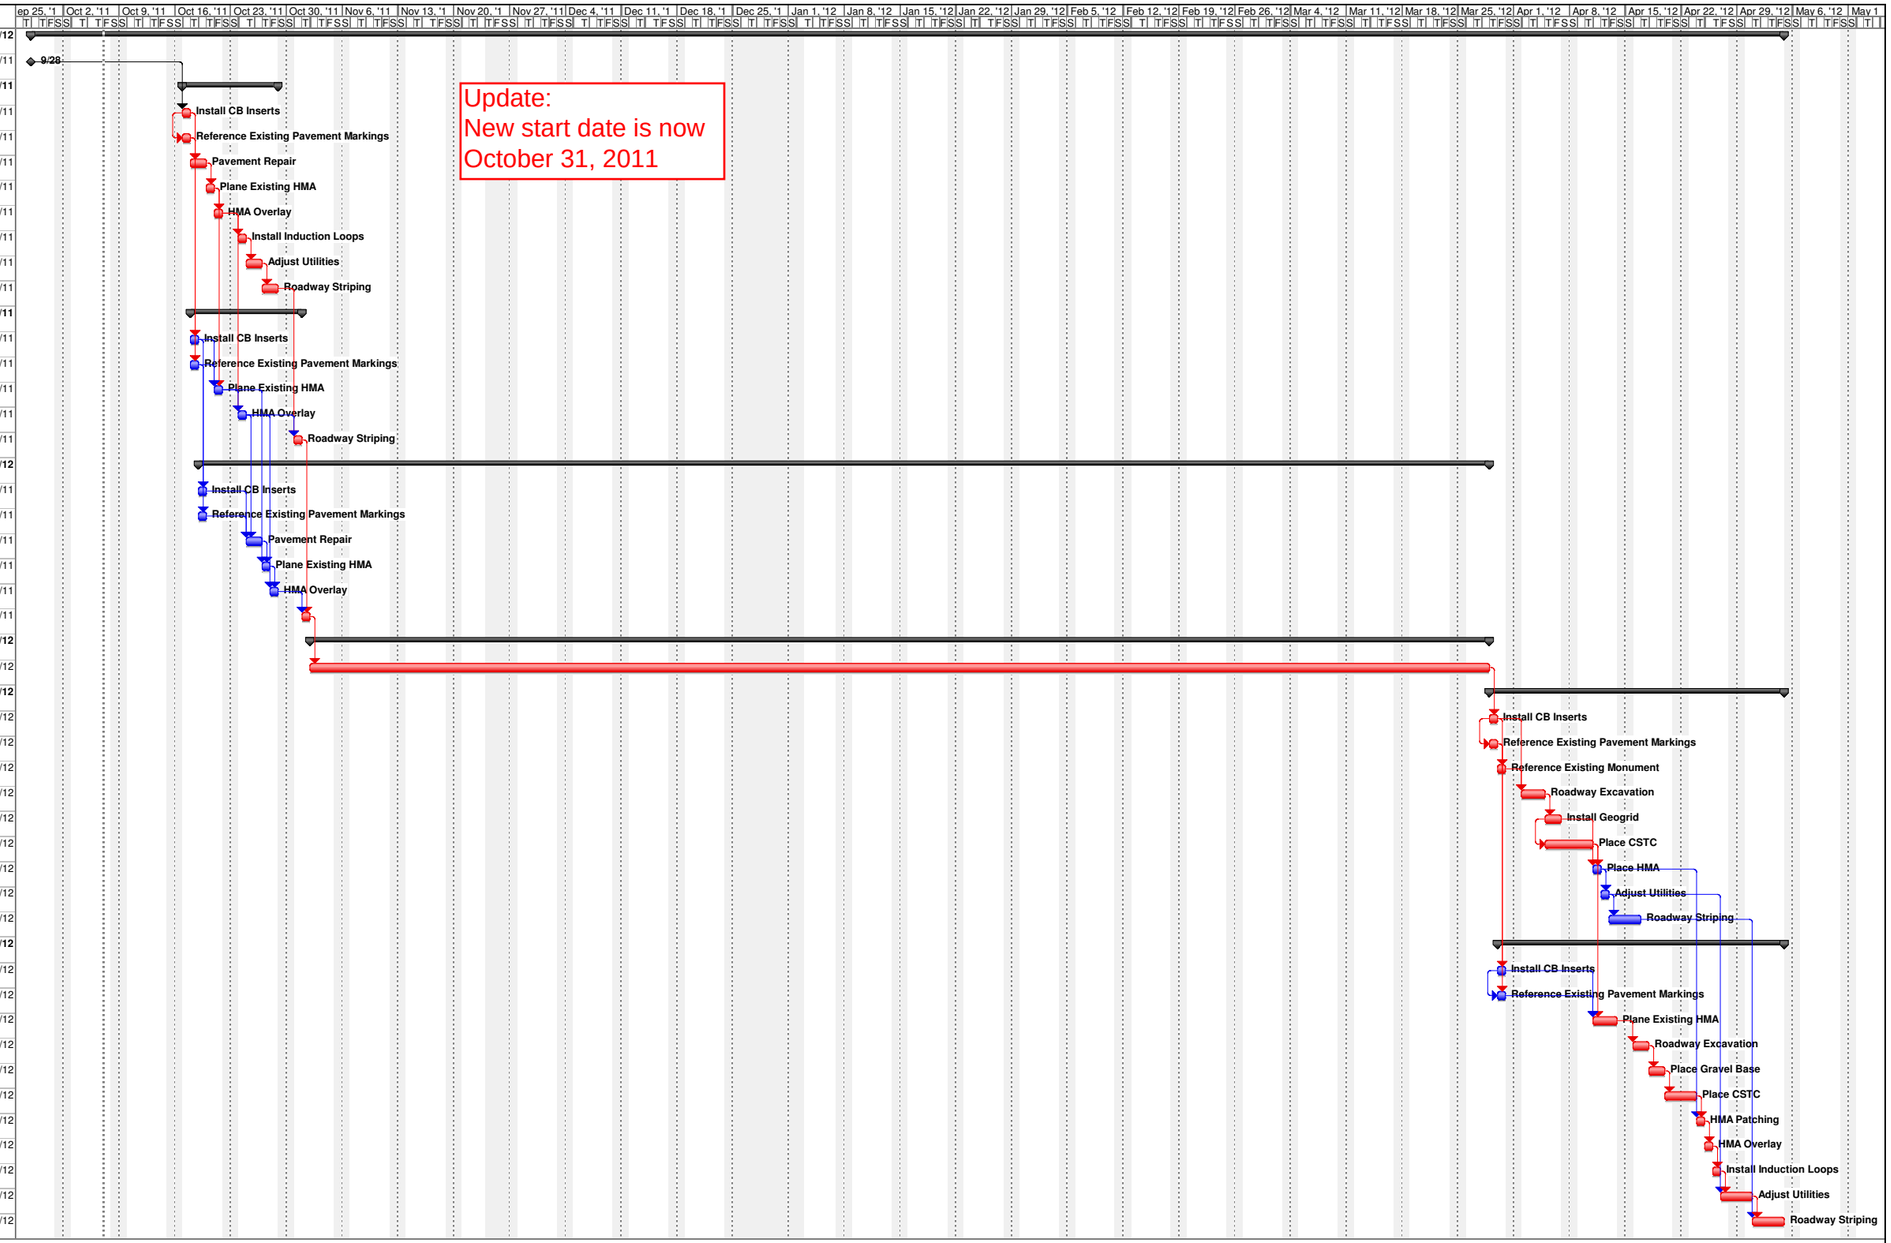

Project: Port Orchard Baseline Schedu
Date: Fri 10/7/11

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | Group By Summary | Deadline
